

Rail control tower | executive decision

Business problem

DERIVED FROM SIMULATED RECORDS: At 2026-08-03, the GBP 311.6m fictional programme has earned 49.0% of its budgeted scope. CPI 0.906, SPI 0.766, cost variance GBP -15.75m and EAC GBP 343.77m. These are demonstration outputs, not real project performance.

Action required

Prioritize S3 possession access and electrification supply review. Its simulated lower productivity and higher cost factor explain weak delivery; this is a designed scenario, not a causal finding from ORR. Confirm access, design and supplier readiness before committing recovery spend. Monitor physical units, weekly earned value, unpaid commitments, overdue actions and forecast movement.


Schedule and recovery

Baseline completion 2027-01-04; current rate extrapolation UNAVAILABLE: stalled packages; recovery UNAVAILABLE: stalled packages. The recovery assumes 25% more weekly production and 8% premium on remaining forecast cost, giving GBP 357.81m EAC. Latest forecastable package finishes 2027-03-22; stalled packages ['S1-3', 'S1-4', 'S2-3', 'S2-4', 'S3-3', 'S4-3', 'S4-4']. An overall finish is unavailable while any incomplete package has zero recent production. Scenario effectiveness has not been observed. Discrete station/signaling quantities make four-week rates volatile. A zero rate returns no finite finish date.

Evidence boundary

OBSERVED CONTEXT: ORR table 3181a supplies 96 railway periods of regional delay rates; table 6320 supplies 79 annual nation records. Context is not used to calibrate simulated project progress. ORR data is licensed OGL v3.0; source Network Rail (infrastructure also TfL and Amey Infrastructure Wales). Source URLs and SHA256 hashes: data/manifest.json.

Earned value control tower DERIVED FROM SIMULATED PROJECT RECORDS

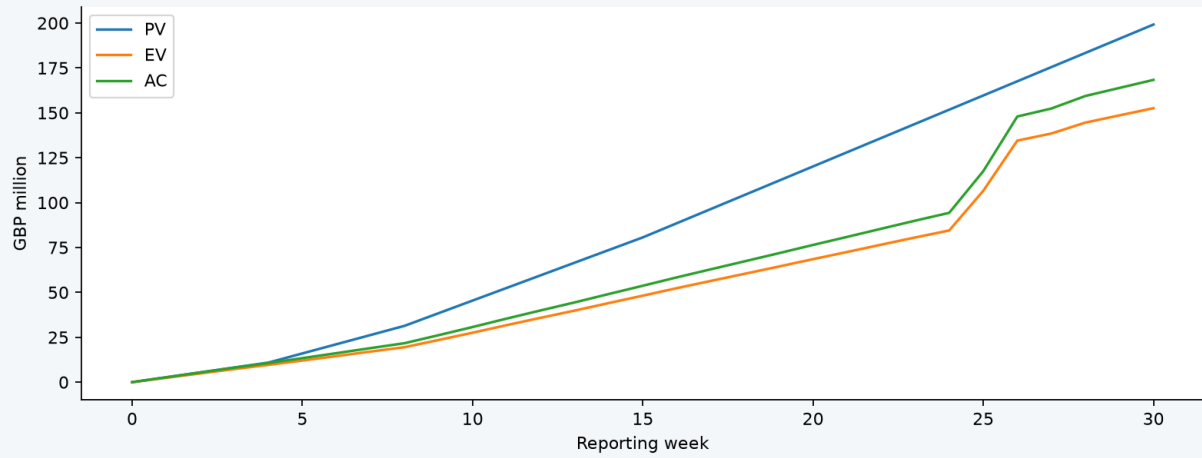

Section cost and schedule efficiency DERIVED FROM SIMULATED PROJECT RECORDS

